
SE LAB -2


NAME :- Keerthi B Patil

SRN:- PES2UG24CS225


SECTION :D

Jira backlog with Epics and User Stories.

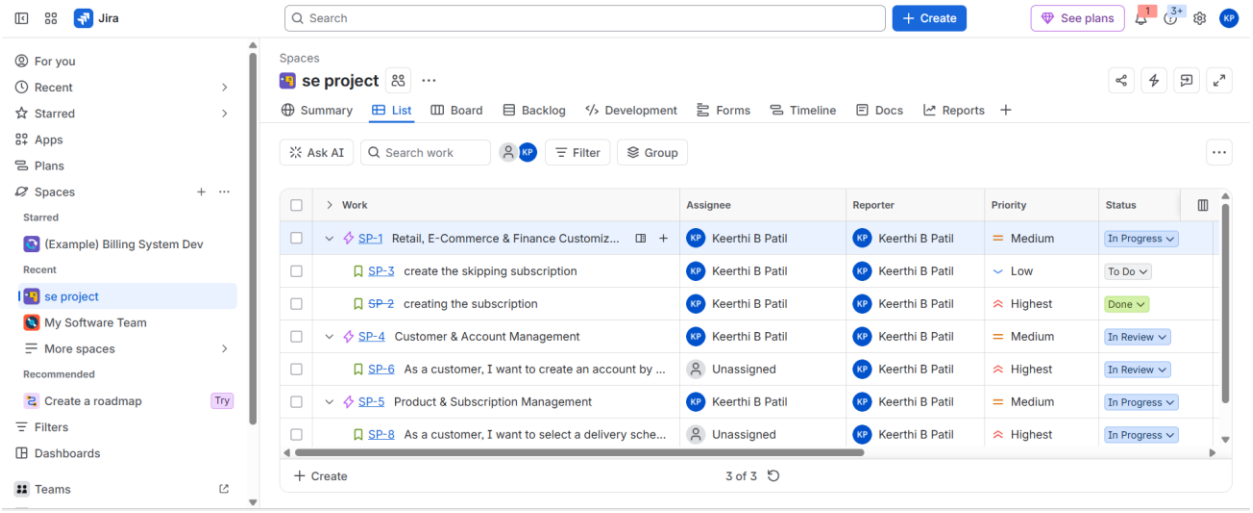


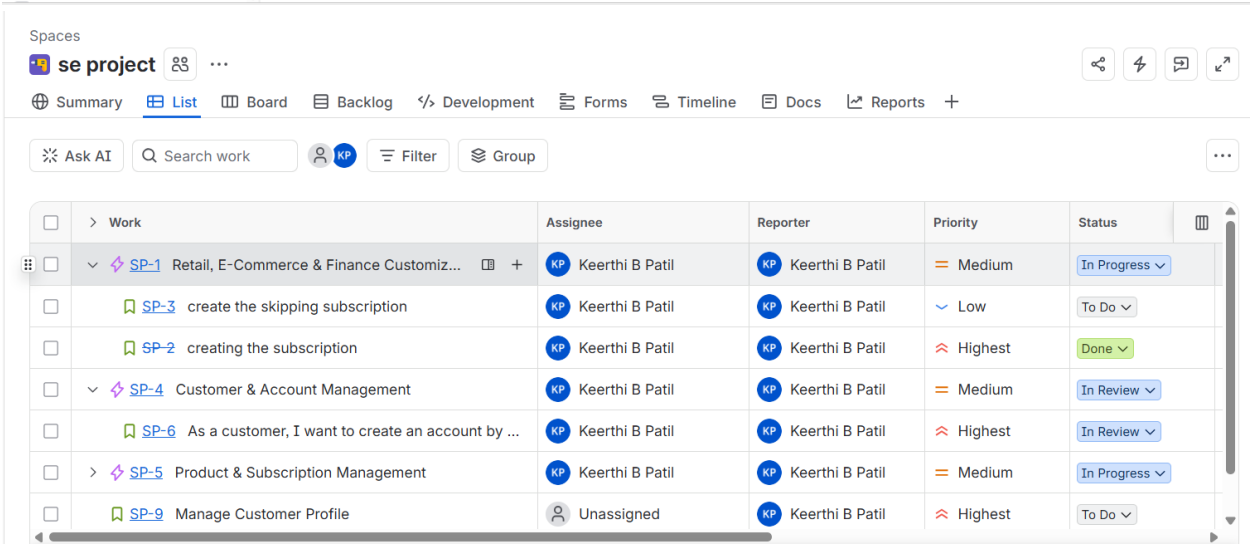


Story point assignments.

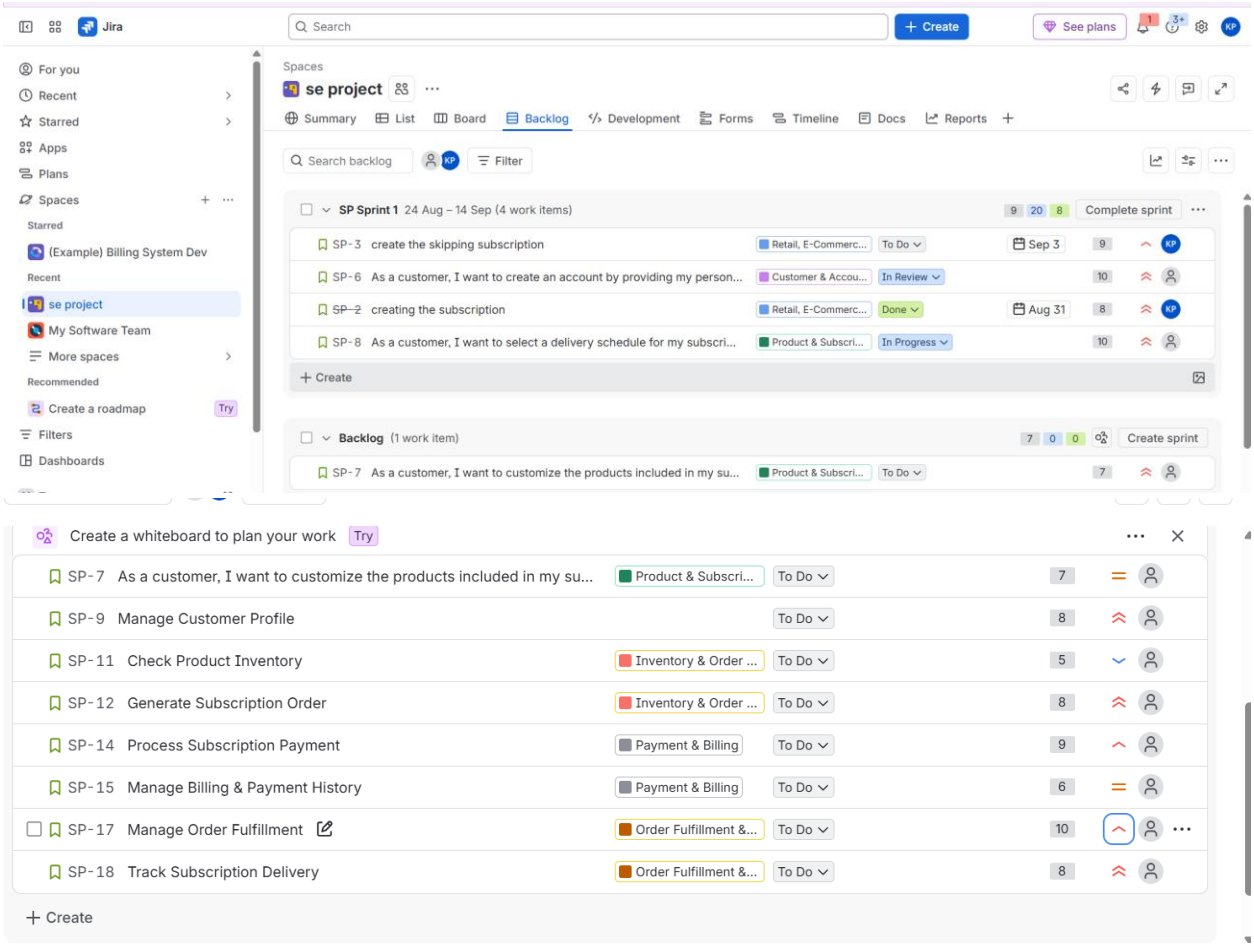


Sprint board (Active Sprint view).

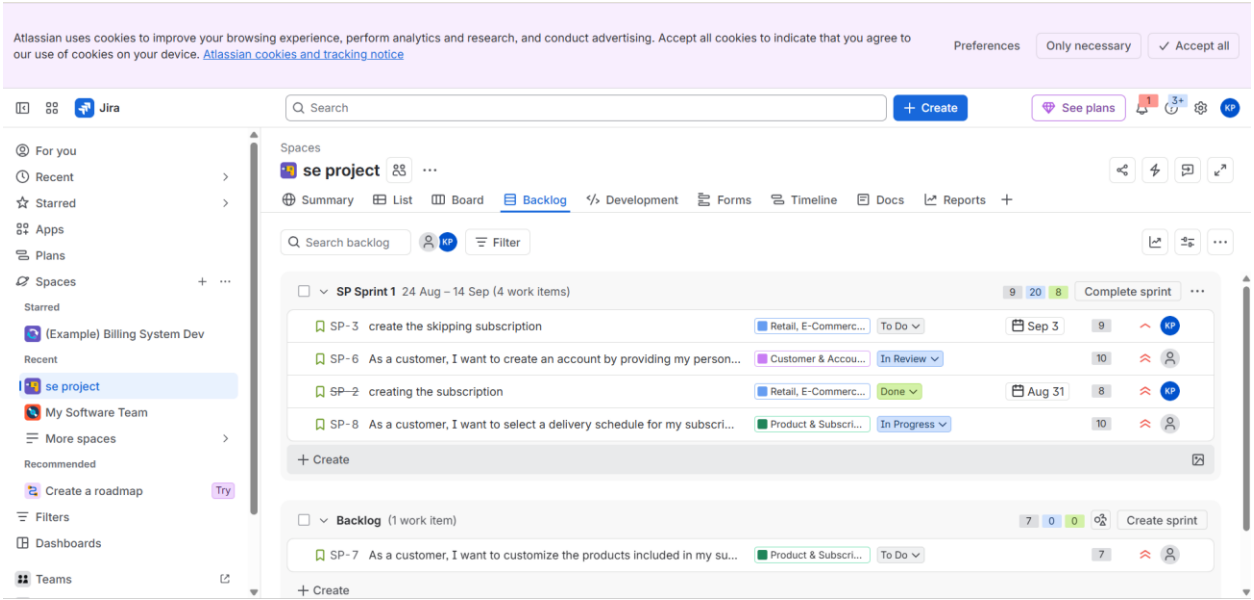

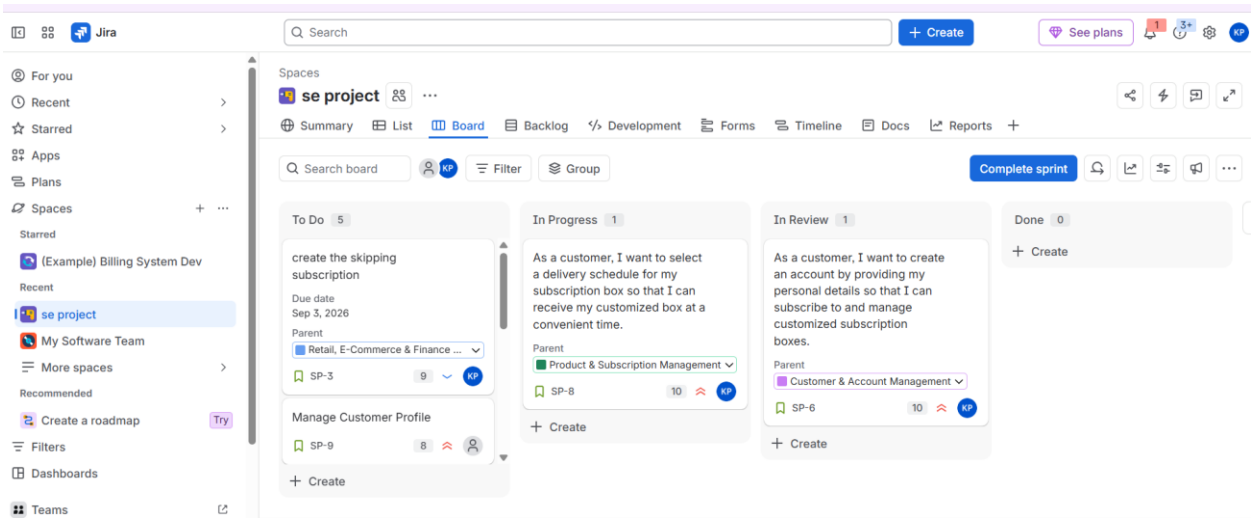

Priority

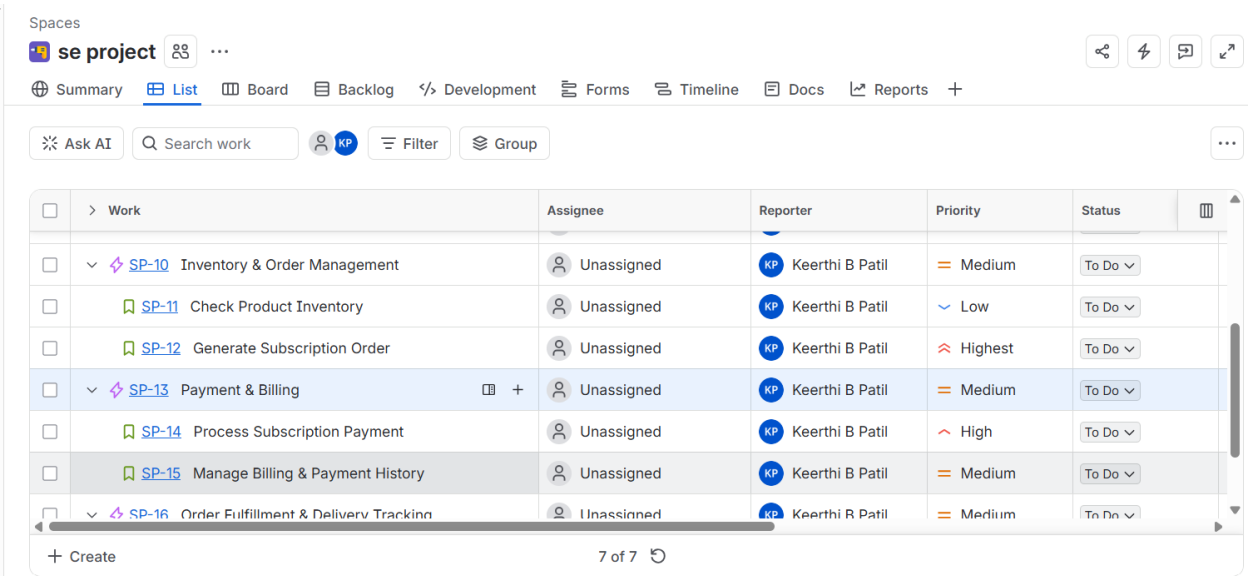

Burndown Chart.



1. Did your estimations reflect the actual effort?
Story points were assigned using the Fibonacci scale **(2, 3, 5, 8)** based on the perceived complexity of each story. Simpler stories such as **Customer Registration** and **Browse Available Products** were given lower story points, while more complex stories such as **Customize Subscription Box**, **Create Subscription Schedule**, and **Generate Subscription Order** were given higher points because they involve multiple requirements and database dependencies. Since this was a simulated sprint rather than an actual development sprint, the estimates were reasonable based on the described complexity, but the actual effort could not be compared with real development time. In a real implementation, **Generate Subscription Order** and **Skip or Reschedule Delivery** could require more effort because they involve scheduling logic, inventory validation, and updating related database records.

2. Was your backlog well-prioritized?
Yes, the backlog was prioritized according to the natural workflow of the **Customizable Subscription Box Scheduler**. The initial stories focused on **customer registration and product browsing**, followed by **box customization and subscription scheduling**. After a subscription is created, the system needs to handle **inventory validation and order generation**, followed by **payment, billing, fulfillment, and delivery tracking**. This ordering ensures that dependent functionalities are implemented only after their required data and processes are available. Core customer and subscription features were given higher priority because they directly support the main objective of the system, while payment, fulfillment, and tracking functionalities were planned after the basic subscription workflow.

3. How did your simulated sprint align with your plan?
The simulated sprint was aligned with the planned backlog because the stories were completed according to their priority and dependencies. The initial work focused on customer and product-related functionality, followed by subscription scheduling, inventory and order management, payment, and delivery tracking. However, since the sprint was simulated and the Jira issues were updated manually, the completion pattern does not represent actual day-by-day development progress. In a real sprint, some stories such as **Customize Subscription Box** or **Generate Subscription Order** might take longer because they depend on multiple database tables and business rules. The simulation therefore helped validate the project plan, but actual development may require adjustments to the schedule and story-point estimates.

4. What insights did the burndown chart give about your team's capacity?
The burndown chart showed how the team's remaining story points changed during the simulated sprint. If the remaining work stayed nearly constant for most of the sprint and then decreased sharply near the end, it indicates that stories were being completed in batches rather than progressively. For the **Customizable Subscription Box Scheduler**, this could mean that several dependent activities, such as **subscription creation, scheduling, inventory checking, and order generation**, were completed together. In a real project, a more gradual decrease would indicate better distribution of work across the sprint. The chart also highlights that complex database-dependent stories should be started earlier to reduce the risk of last-minute workload and ensure that the team can complete the sprint within its planned capacity.
